

## Pictometry Weekly Status Report

**Project Name:** LARIAC3

**Report Date:** 7/19/2011

**Report Number:** 27

**Prepared By:** Katie Neal-Vacca

**Current Status:**

Flight Planning: Completed

Data Acquisition: Image Capture Complete

Scheduled Flight Plans: Complete

Finished Flying: All Image Capture Complete

**Scheduled Work:**

Data acquisition for AT blocks #1-29

Initial Processing starting for #1-29

Blocks 13, 14, 15, 16, 17, 18, 23, 24, 25, and 26 are 100% complete; Blocks 1, 2, 4, 5, 12, and 27 are 95% complete; Blocks 3, 6, 7, 8, 9, 10, 11, and 22 are 85% complete; Blocks 20 is 70% complete; Block 21 is 35% complete, Blocks 19 is 15% complete.

**AT Blocks:**


Imagery Sent to Sanborn: 1, 4, 5, 11-18, 23-27

Blocks Pending Approval from Dewberry: 1, 2, 4, 12


Blocks Accepted by Dewberry: 13-18, 23-27

Imagery Acquisition Complete

## LAR-IAC3 Imagery Acquisition - Complete

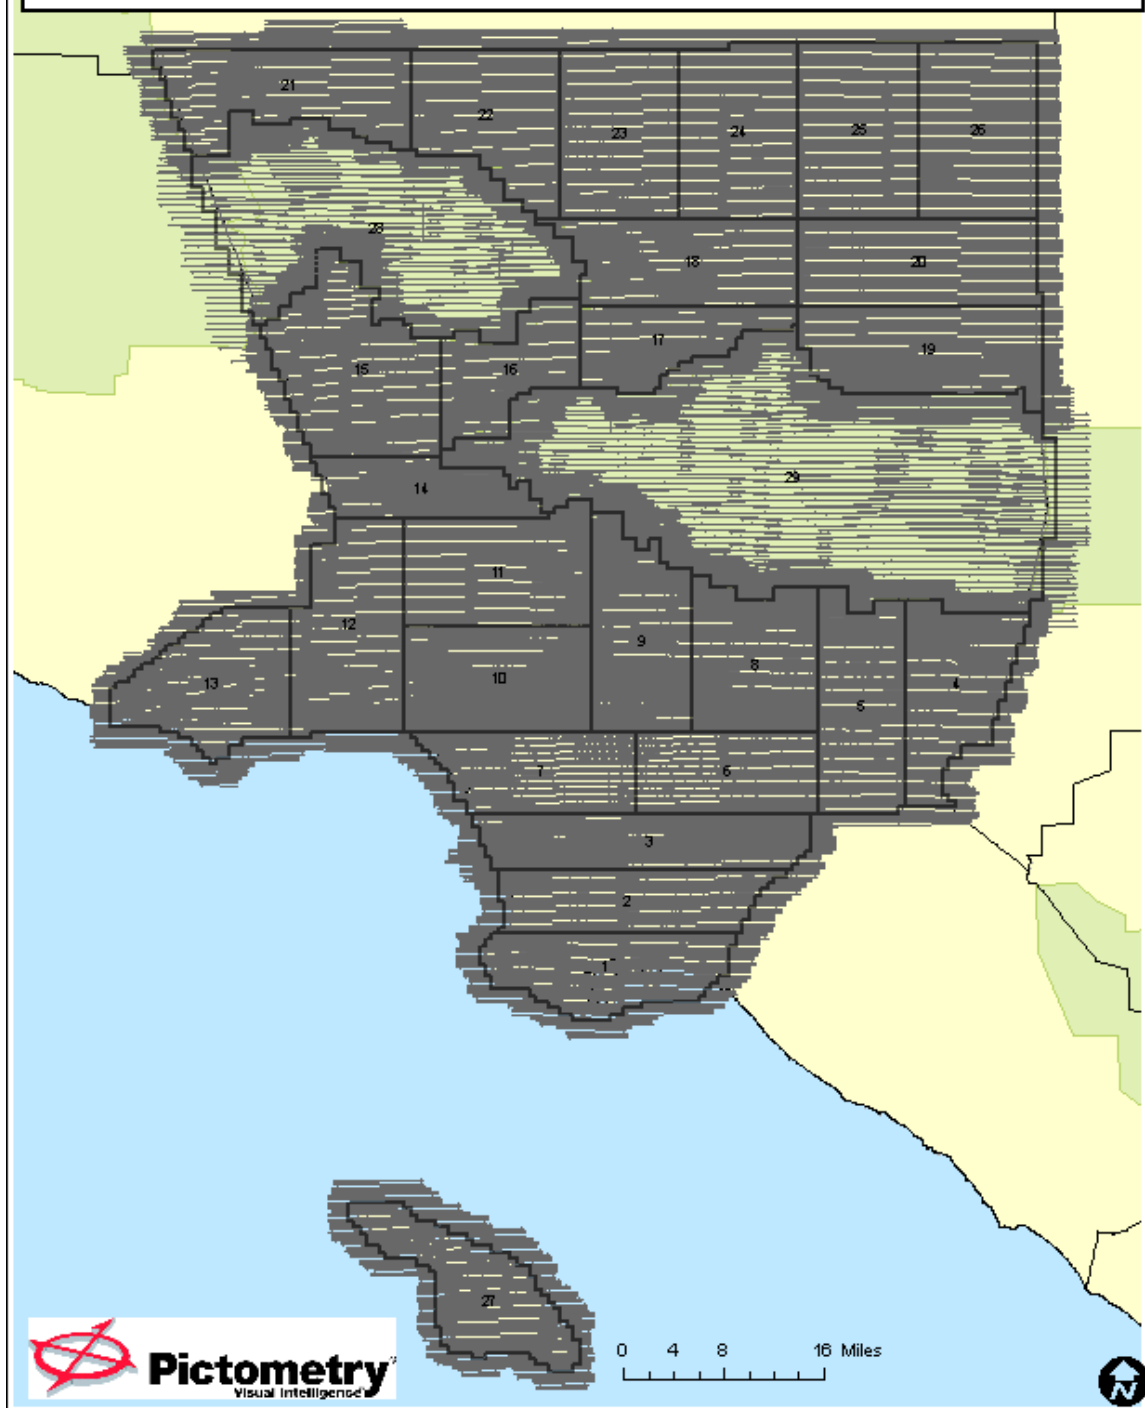


# LAR-IAC3 AT - 20110719

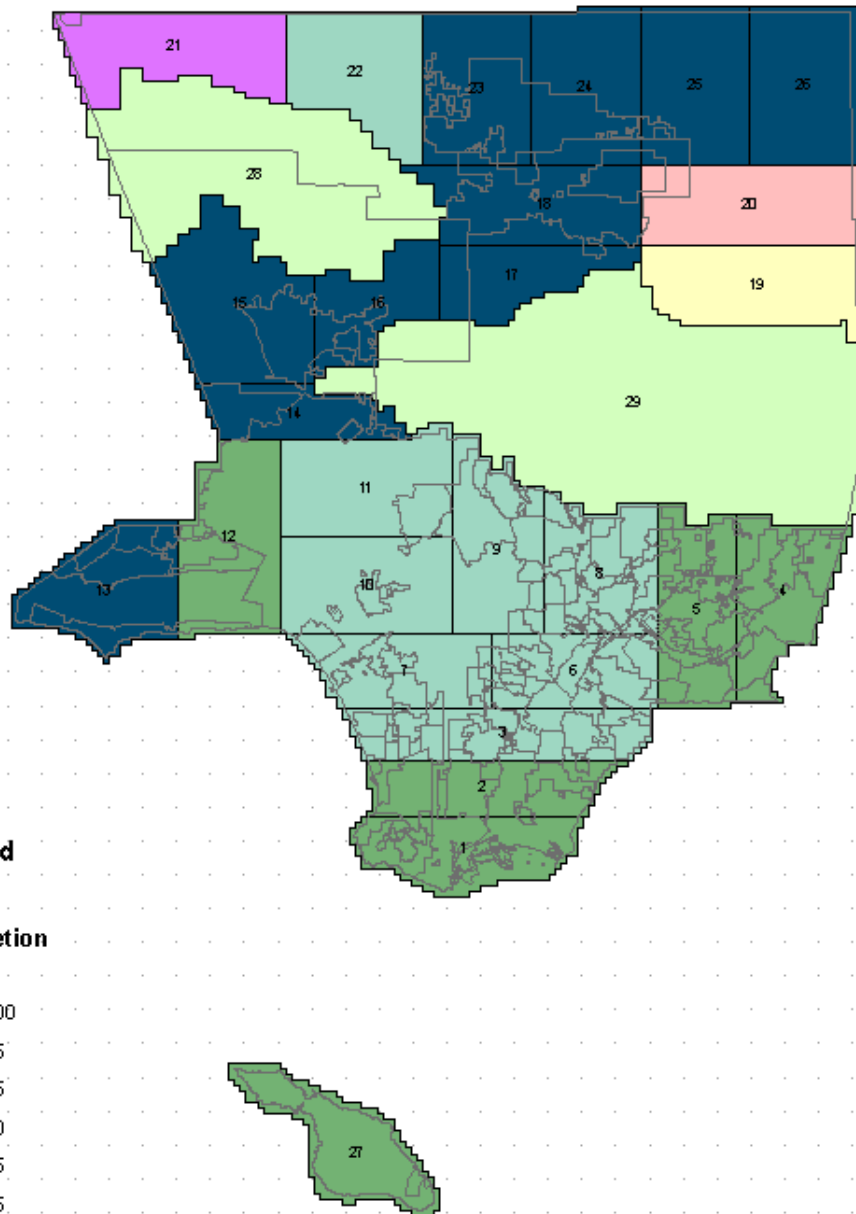

## Legend

AT

Completion




### Estimated Schedule-

AT Block	Estimated AT Delivery Date	Updated AT Delivery Date	AT Delivery	AT Approval	Estimated Tile Delivery	Updated Tile Delivery	Final Tile Delivery
1	6/17/2011	7/1/2011	7/1/2011		9/15/2011	10/17/2011	
2	6/24/2011	7/8/2011	7/8/2011		9/30/2011	10/17/2011	
3	6/24/2011	7/8/2011			9/30/2011	10/31/2011	
4	6/24/2011		6/24/2011		10/17/2011	10/17/2011	
5	7/1/2011	7/22/2011			10/17/2011	10/31/2011	
6	7/1/2011	7/22/2011			10/17/2011	11/15/2011	
7	7/1/2011	7/22/2011			10/31/2011	11/15/2011	
8	7/8/2011	7/22/2011			11/15/2011	11/15/2011	
9	7/8/2011	7/22/2011			11/15/2011	11/30/2011	
10	7/1/2011	7/22/2011			10/31/2011	11/30/2011	
11	7/1/2011	7/22/2011			10/31/2011	11/30/2011	
12	5/27/2011	6/24/2011	6/24/2011		9/15/2011	9/30/2011	
13	5/20/2011	5/25/2011	6/2/2011	6/18/2011	8/31/2011	9/30/2011	
14	5/27/2011	6/17/2011	6/20/2011	7/7/2011	9/30/2011	10/10/2011	
15	5/20/2011	5/24/2011	6/2/2011	7/7/2011	8/15/2011	10/10/2011	
16	5/20/2011	5/24/2011	6/2/2011	7/7/2011	8/15/2011	10/17/2011	
17	5/20/2011	5/24/2011	6/2/2011	7/7/2011	9/15/2011	10/17/2011	
18	5/17/2011		5/17/2011	5/25/2011	8/15/2011	9/15/2011	
19	6/10/2011	7/29/2011			10/17/2011	11/30/2011	
20	6/10/2011	7/29/2011			9/15/2011	12/15/2011	
21	6/3/2011	7/29/2011			11/15/2011	12/15/2011	
22	5/27/2011	7/29/2011			9/30/2011	12/15/2011	
23	Accepted			5/17/2011	8/15/2011	9/15/2011	
24	Accepted			5/17/2011	8/31/2011	9/15/2011	
25	Accepted			4/18/2011	8/15/2011		
26	Accepted			4/18/2011	8/15/2011		
27	6/3/2011	7/20/2011	7/1/2011	7/12/2011	11/15/2011	10/31/2011	
28	7/8/2011				11/30/2011		
29	7/8/2011				11/30/2011		

### Ortho Tile Update –

Project Phase	% Completed This Period	% Completed Previous Periods	Total % Completed	Comments
Project Setup and Initiation	100%	95%	100%	Sanborn internal documentation in process (charter, specification documentation, work plan) DEM restored Tile grid renamed
Orthoimagery production	16%	13%	16%	Ortho production for AT blocks 13, 18, 23-26
Delivery	>1%	0%	>1%	Sample tiles provided for approval of color balance.

# LARIAC3 Ortho Delivery Blocks Status as of July 18, 2011

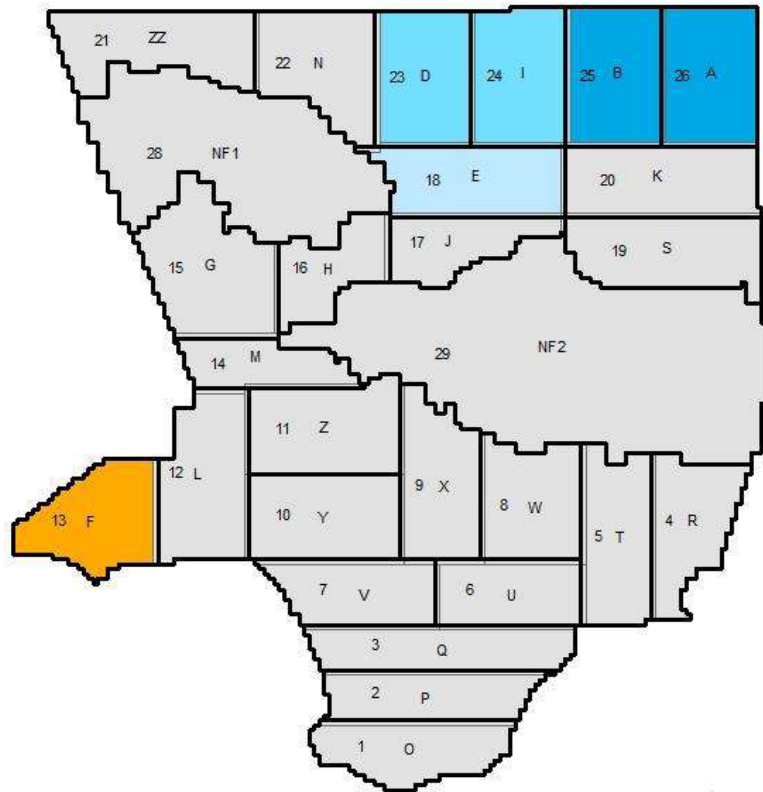

## LARIAC3\_OrthoDeliveryBlocks

### Phase, Status

- , Not Started
- Edit/QC, 10%
- Edit/QC, 20%
- Edit/QC, 50%
- Rectification, 10%

